


**SITE PLAN FOR MANUFACTURED HOME PARKS**

<b>EXISTING BASE SUPPORT</b>
PIERS _____
SPACING _____
SLAB _____
SIZE _____
RUNNERS MIN. 24" WIDE SPACING _____
CROSS RUNNERS MIN. 24" WIDE SPACING _____

<b>NEW BASE SUPPORT</b>
ALL CONCRETE 3000 P.S.I. MIN.
PIERS _____ 24" x 36" D.
SLAB _____ 6"D x W. x L. OF HOME
RUNNERS _____ 24"W. x 6"D.
CROSS RUNNERS _____ 24"W. x 6"D. x 8' MAX
ABS PADS _____ 24" x 24"/6" COMPACTED STONE

<b>TIE DOWNS</b>
AUGERS/STRAPS 45° ANGLE _____
MINUTE MAN _____
OLIVERS _____
LAG TO SILL _____

<b>FLOOD PLAIN</b>
YES ___ NO ___
<i>*OLIVERS ARE THE ONLY TIE DOWNS APPROVED FOR FLOOD PLAIN</i>

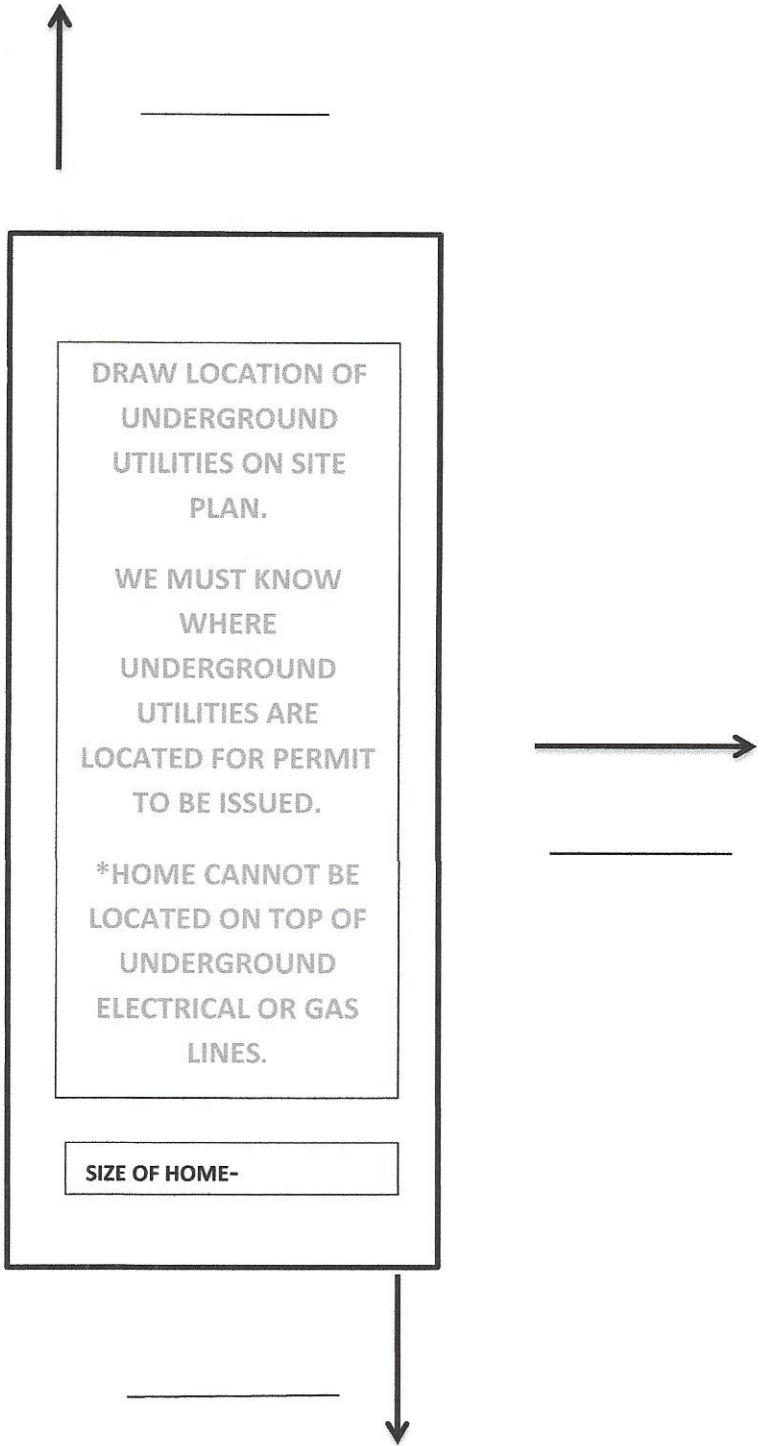

**\*Measure to the nearest home, street or property line from where the home will be set.**

Park Address and lot #: \_\_\_\_\_ ODOC INSTALLER SETTING HOME: \_\_\_\_\_

**\*AREA UNDER HOME MUST BE CROWNED, ALL BASE SUPPORT TO BE ABOVE GRADE. SLABS, RUNNERS, CROSS RUNNERS AND PIERS MAY REQUIRE REBAR, IF SO 3/8 INCHES MINIMUM REBAR MUST BE USED.**
